Appendix 2 - Programme for implementation of Heating Policy

ID	Task Name	Duration	Start	Finish
1				
2	**Heating Policy Programme**	**211 days**	**Fri 08/12/23**	**Mon 30/09/24**
3	Engineering Team commence development of Heating Policy	0 days	Fri 08/12/23	Fri 08/12/23
4	Develop Heating Policy	36 days	Fri 08/12/23	Fri 26/01/24
5	Draft version of Heating Policy issued for comments within P&FM	0 days	Fri 26/01/24	Fri 26/01/24
6	Finalise governance / strategy for implementation	10 days	Mon 29/01/24	Fri 09/02/24
7	Incorporate P&FM comments	5 days	Mon 12/02/24	Fri 16/02/24
8	Draft version of Heating Policy issued for consultation	0 days	Mon 19/02/24	Mon 19/02/24
9	Consultation period	25 days	Mon 19/02/24	Fri 22/03/24
10	Develop Heating Policy - incorporate comments from consultation process	5 days	Mon 25/03/24	Fri 29/03/24
11	Final version of Heating Policy complete	0 days	Fri 29/03/24	Fri 29/03/24
12	Prepare Committee reports	62 days	Mon 04/03/24	Tue 28/05/24
13	Strategic Leadership Team Meeting	0 days	Wed 06/03/24	Wed 06/03/24
14	Banff & Buchan and Marr Area Committee Meetings	0 days	Tue 16/04/24	Tue 16/04/24
15	Buchan and Garioch Area Committee Meetings	0 days	Tue 23/04/24	Tue 23/04/24
16	Formartine and Kincardine & Mearns Area Committee Meetings	0 days	Tue 30/04/24	Tue 30/04/24
17	Sustainability Committtee Meeting	0 days	Wed 22/05/24	Wed 22/05/24
18	Business Services Committee Meeting	0 days	Thu 13/06/24	Thu 13/06/24
19	Heating Policy introduction phase / Council-wide communications	76 days	Fri 14/06/24	Fri 27/09/24
20	Heating Policy development & implementation complete	0 days	Mon 30/09/24	Mon 30/09/24

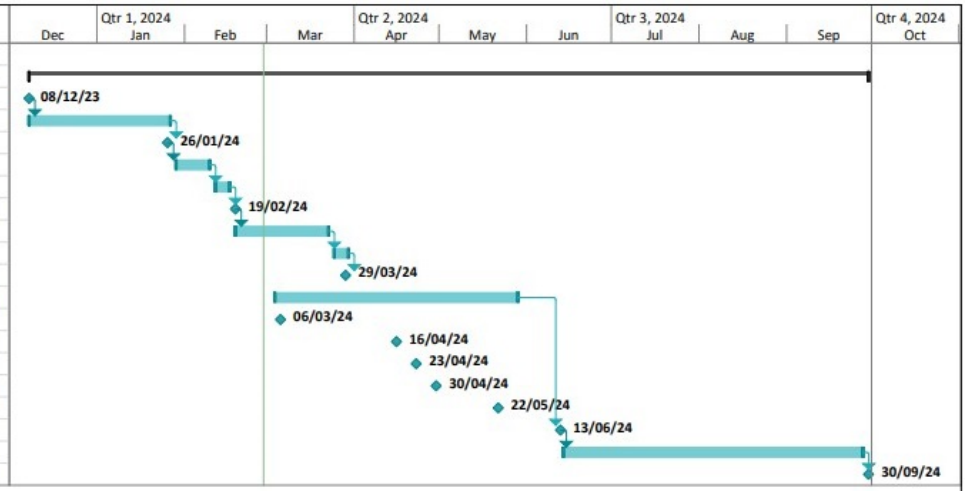

Project: Heating Policy Programm
Date: Thu 29/02/24

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
Summary		Inactive Task		Duration-only		Finish-only			
